
OC Streetcar Project Update







Transit Connectivity

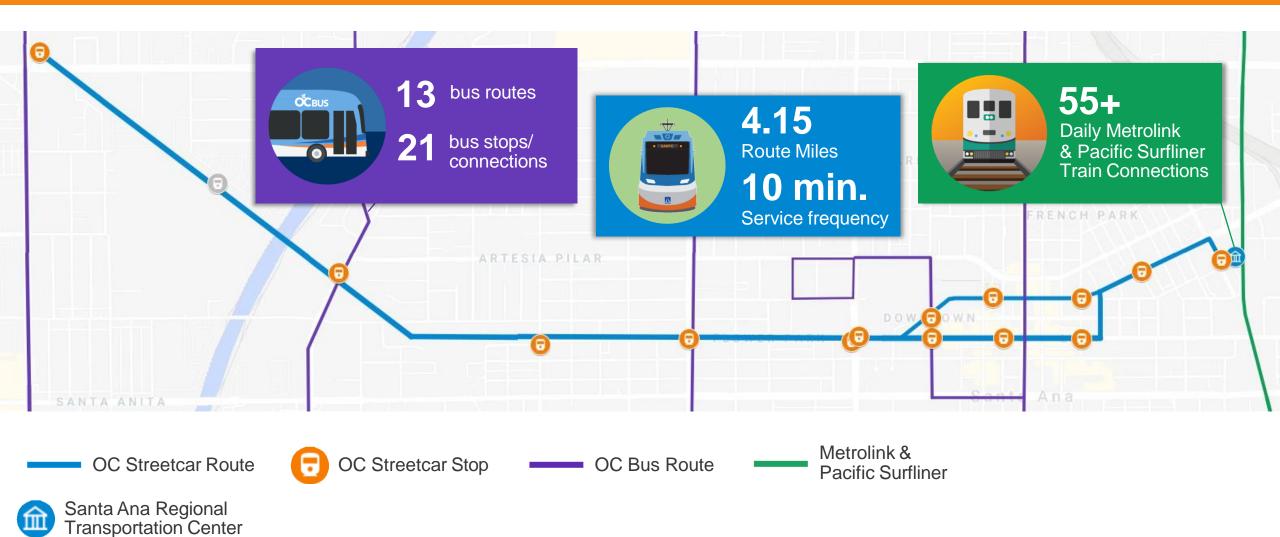

OC Streetcar Segments 1 to 5

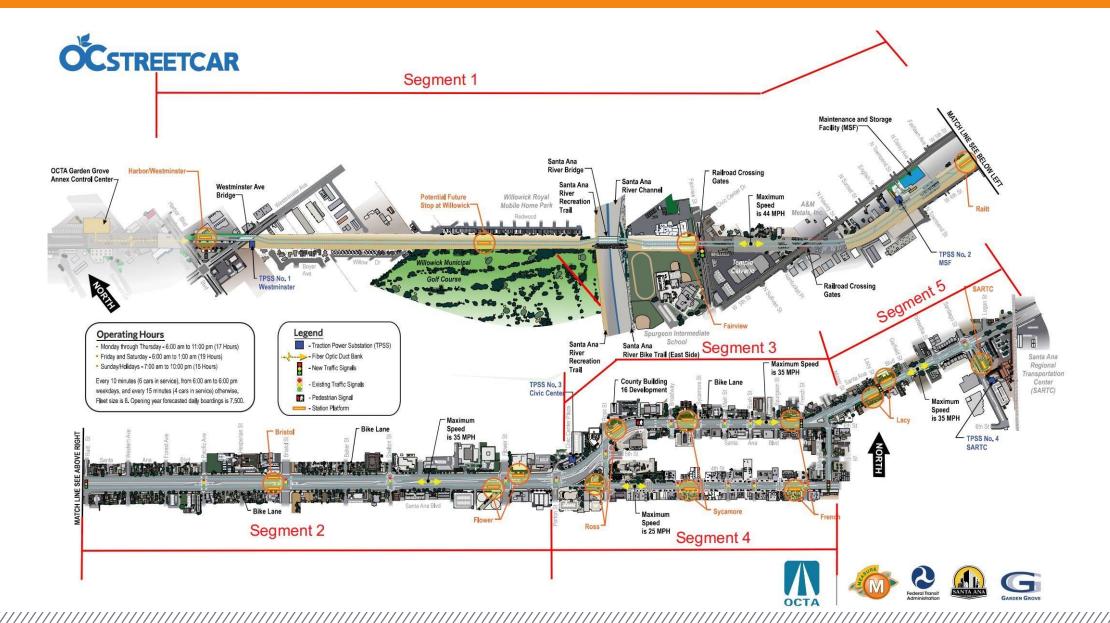


Construction – Segment 1

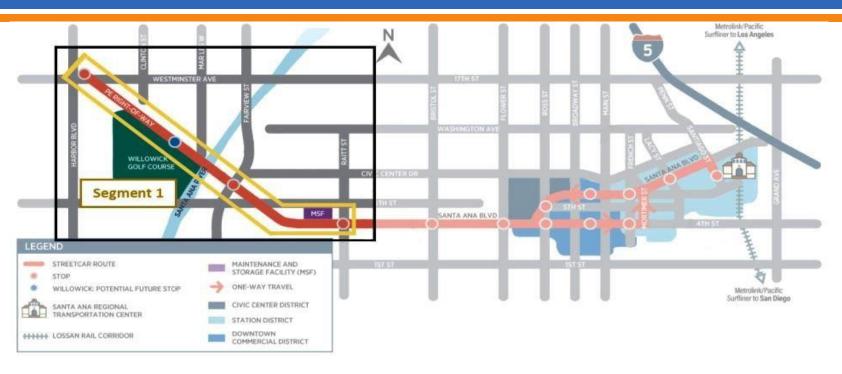


- Pacific Electric Right-of-Way (PEROW)
 - Substantial completion of the Santa Ana River and Westminster bridges, and Harbor Station Platform with ongoing placement of concrete plinths and rails.
- Maintenance and Storage Facility
 - Construction continues and includes remaining installation of exterior walls and roof insulation, conduit and piping, girder painting, other interior improvements, and tracks.

Harbor Station Platform

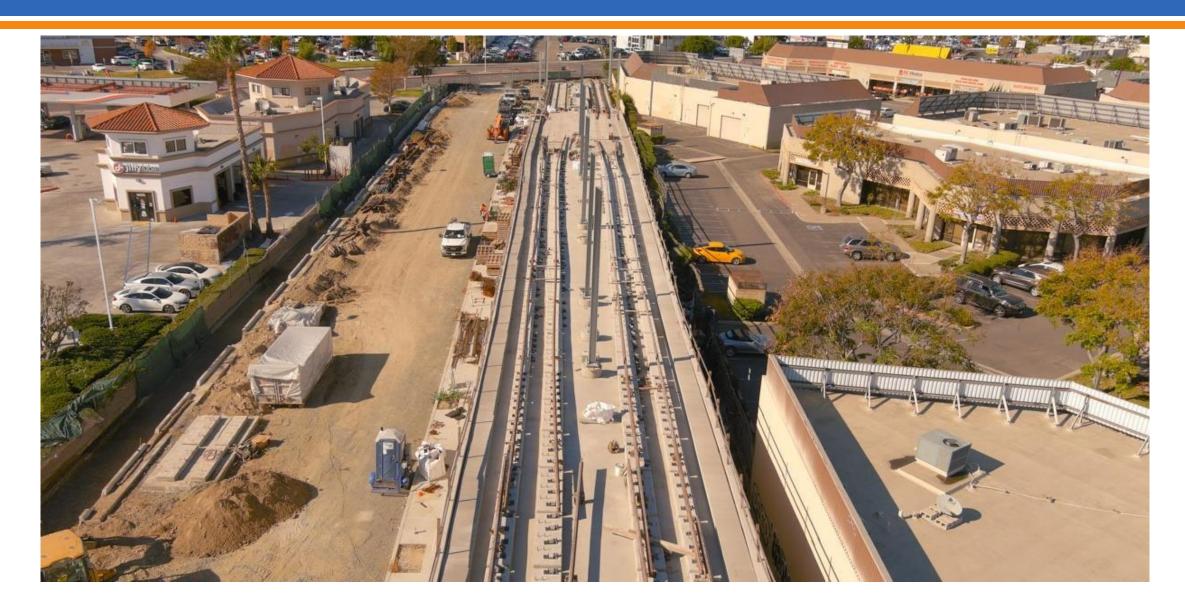

Westminster and Santa Ana River Bridges



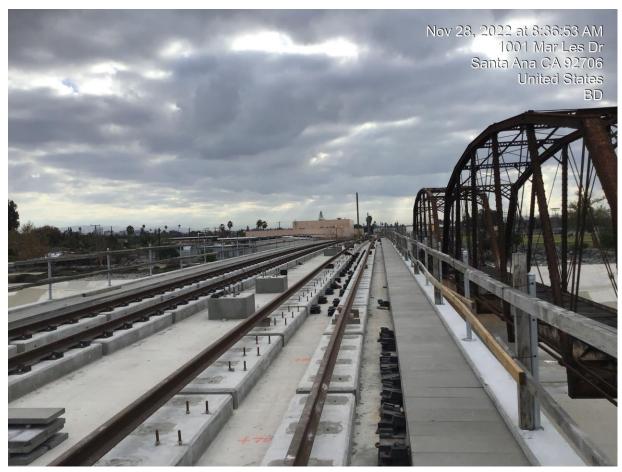

Westminster Bridge Plinths

Santa Ana River Bridge Plinths

Maintenance and Storage Facility




Maintenance and Storage Facility (Cont.)




Exterior Walls

Tracks within the Service and Inspection Pit

Maintenance and Storage Facility (Cont.)

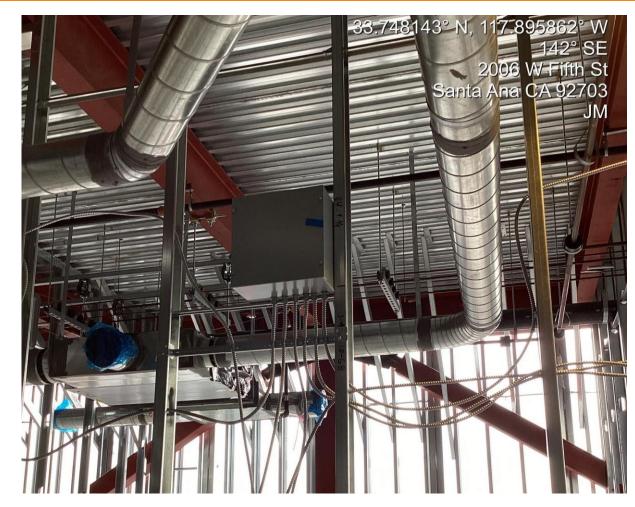


Interior Walls, Piping and Heating, Ventilation, and Air Conditioning

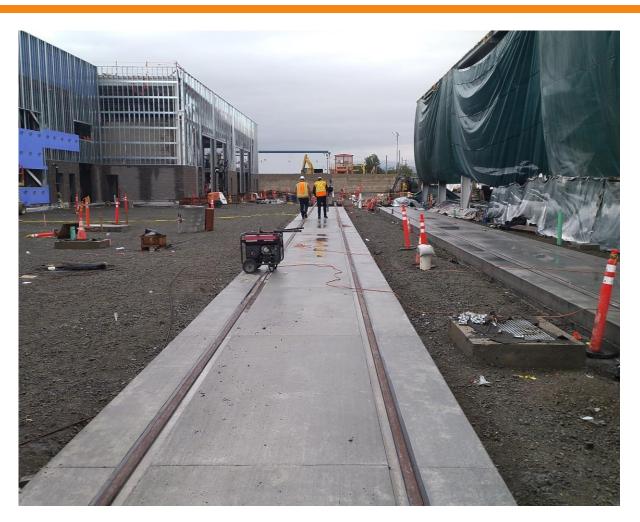

Embedded Track

Construction – Segments 2 through 5

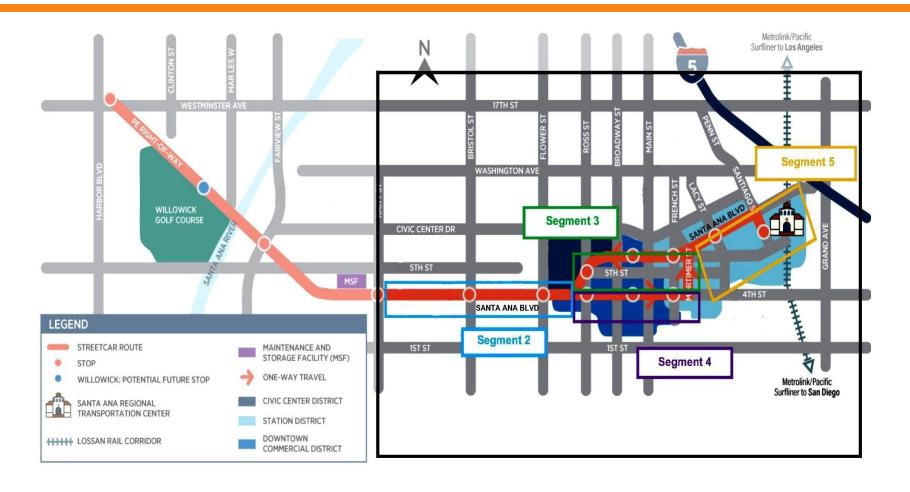

• Key completions in Segments 2, 3, 4, and 5

Progress on Segment 2B







Bristol Street to Flower Street

Bristol Side Station Platforms

Progress on Segment 4 (Fourth Street)

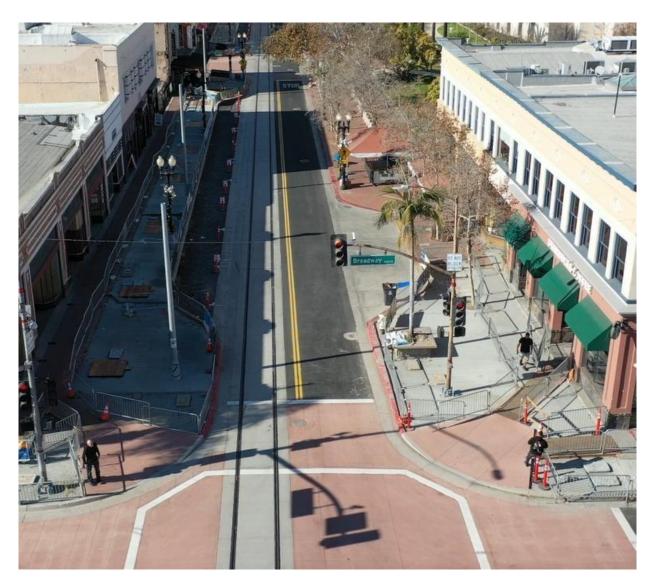

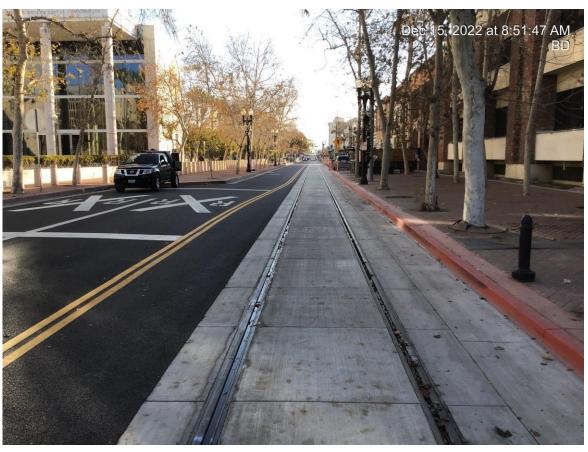


Between Broadway and Ross Street


Fourth Street Station Platform





Platform & Vehicle Access

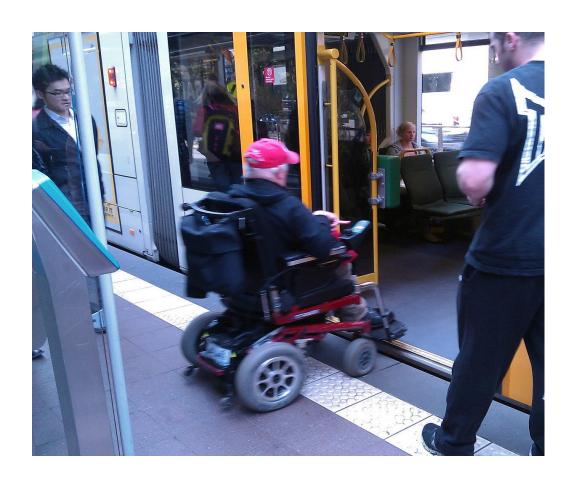

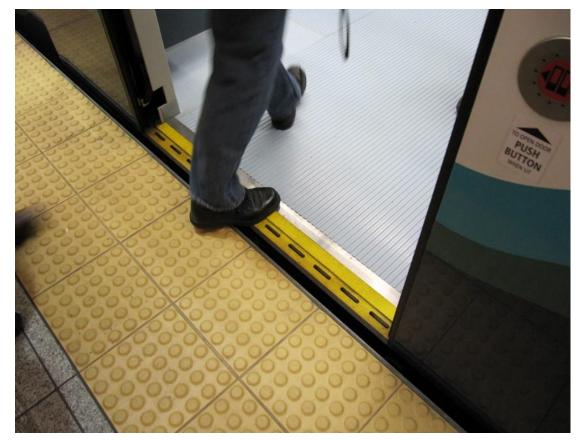


Progress on Segment 5



Embedded Track – Near Garfield Street



Track Installation Progress

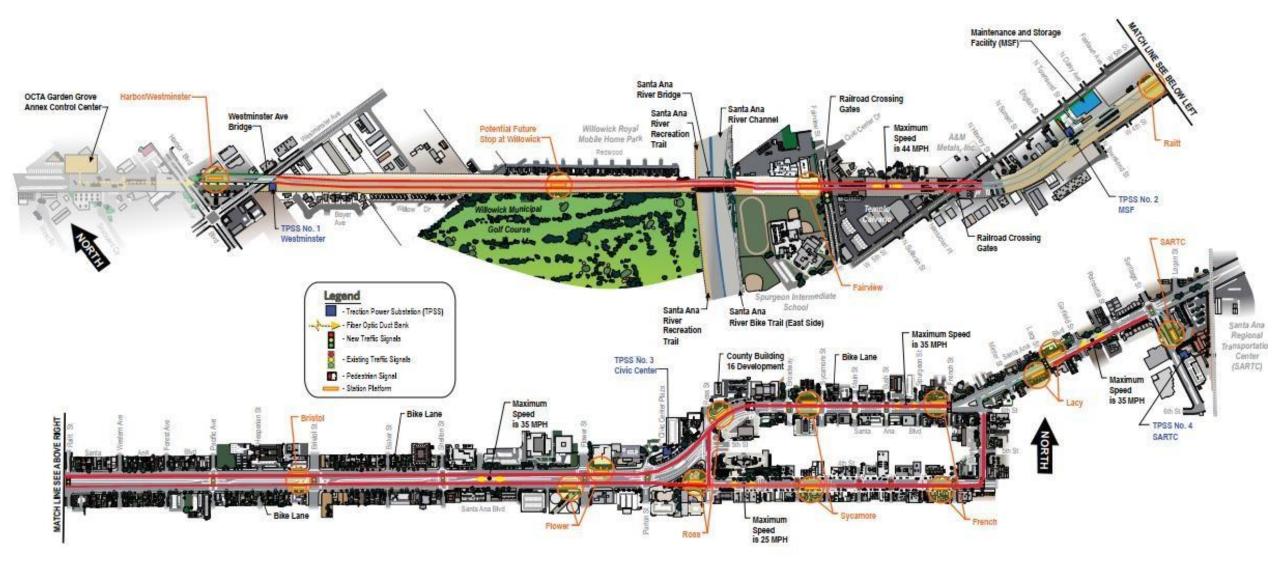

Upcoming Construction Activities

- Segment 1 Complete track work on bridges and within PEROW.
- Maintenance and Storage Facility Continue site and building work to ensure significant completion for vehicle storage. Start track work to building.
- Segment 2 Significantly complete the remaining work, including asphalt concrete paving and start conditional acceptance with City of Santa Ana (City) staff.
- Segment 4 Complete installation of pavers, electrical, and overhead contact system items.
 Continue conditional acceptance with City staff.
- Segment 5 Start trackwork in westbound direction. Continue excavation for Santa Ana Regional Transportation Center station. Start work at Santiago Street intersection.
- Continue station platforms at various locations.
- Installation of new traffic signal poles at many intersections.
- Installation of remaining overhead catenary system poles.
- Installation of Traction Power Substations.

Vehicles

- Cars 1-7 are in the final stages of manufacturing with installation of the last remaining vehicle components.
 - Most of the action items from the First Article Inspection of Car 1 were signed off at reinspection with remaining items to be closed in early 2023.
 - Car 8 is in final assembly and preparations are underway to commence static and dynamic testing in first quarter 2023.
- Staff returned to Siemens in December 2022 to inventory and approve additional items and discuss the vehicle delivery schedule and warranty extension for spare parts and special tools.






Public Outreach Program

- Fourth Street Business Outreach
- City Council
- Field Meetings
- Door-to-Door Outreach
- **Downtown Business Associations**
- Eat Shop Play Program
- **Construction Alerts**



- **Crowd Fence Covers**
- Parking Structure Banners
- Eat Shop Play Banners
- Wayfinding Banners
- Newspaper, Radio, and Spotify Ads

Eat, Shop, Play Advertisement Video






Santa Ana River Bridge



Ballast Tracks within the PE ROW

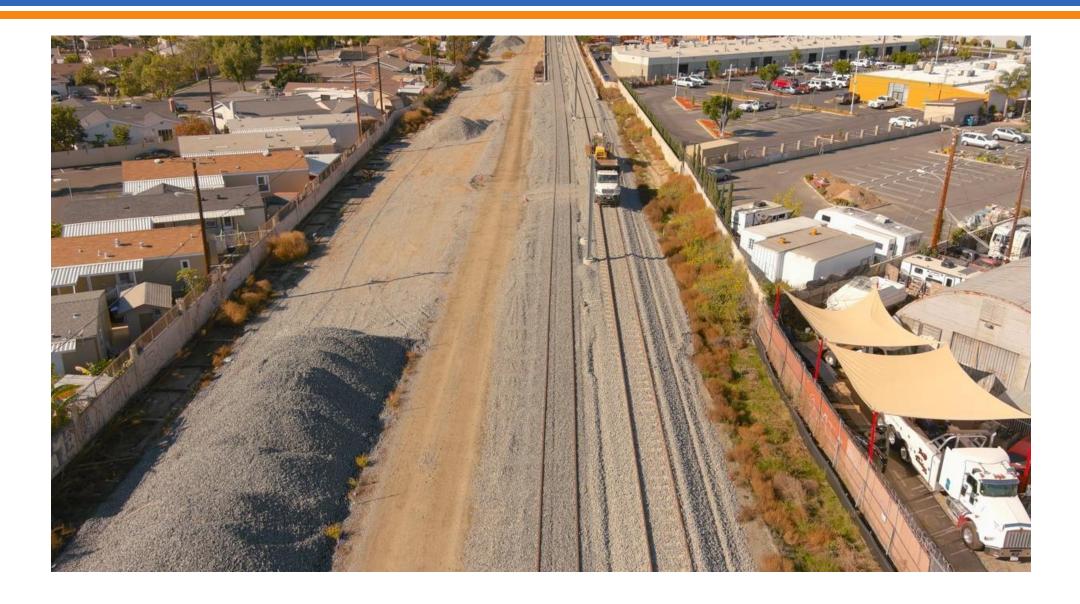

Progress on Segment 3

