



Construction Notification

Week of April 15, 2019

Crews have substantially completed the tree removals. Sewer installation work along the project route continues, with work generally moving from west to east. Sewer installation activities include excavation, trenching, installation of sewer pipelines, and road work and restoration. Sewer installation work requires temporary parking and lane restrictions.

Additionally, crews will begin water pipeline work on April 22, which requires temporary lane and sidewalk restrictions. Advance notice will be provided to community members in the segment prior to the start of this work.

Access will be maintained for all residents and businesses.

For specific work activities in your area, see the segment overviews and maps below. All scheduled activities are weather permitting and are subject to change.

SEGMENT 1 CONSTRUCTION ACTIVITIES


Intersection of Harbor Blvd. and Westminster Ave. to Raitt St.

Over the next two weeks, Segment 1 construction activities will include:

- Preliminary work and demolition at the site of the future Maintenance Storage Facility
- Tree removal and tree stump grinding within the Pacific Electric Right-of-Way (PEROW)
- Water pipeline work within the PEROW, adjacent to Westminster Avenue

Water pipeline work will require a temporary single-lane closure on Westminster Avenue, as well as a sidewalk closure on the south side of Westminster Avenue adjacent to the PEROW. Please slow through the construction area. Advance notice will be provided to community members in the segment prior to the start of this work.

Following project completion, trees will be replanted along the OC Streetcar alignment. More trees will be replanted than will be removed.

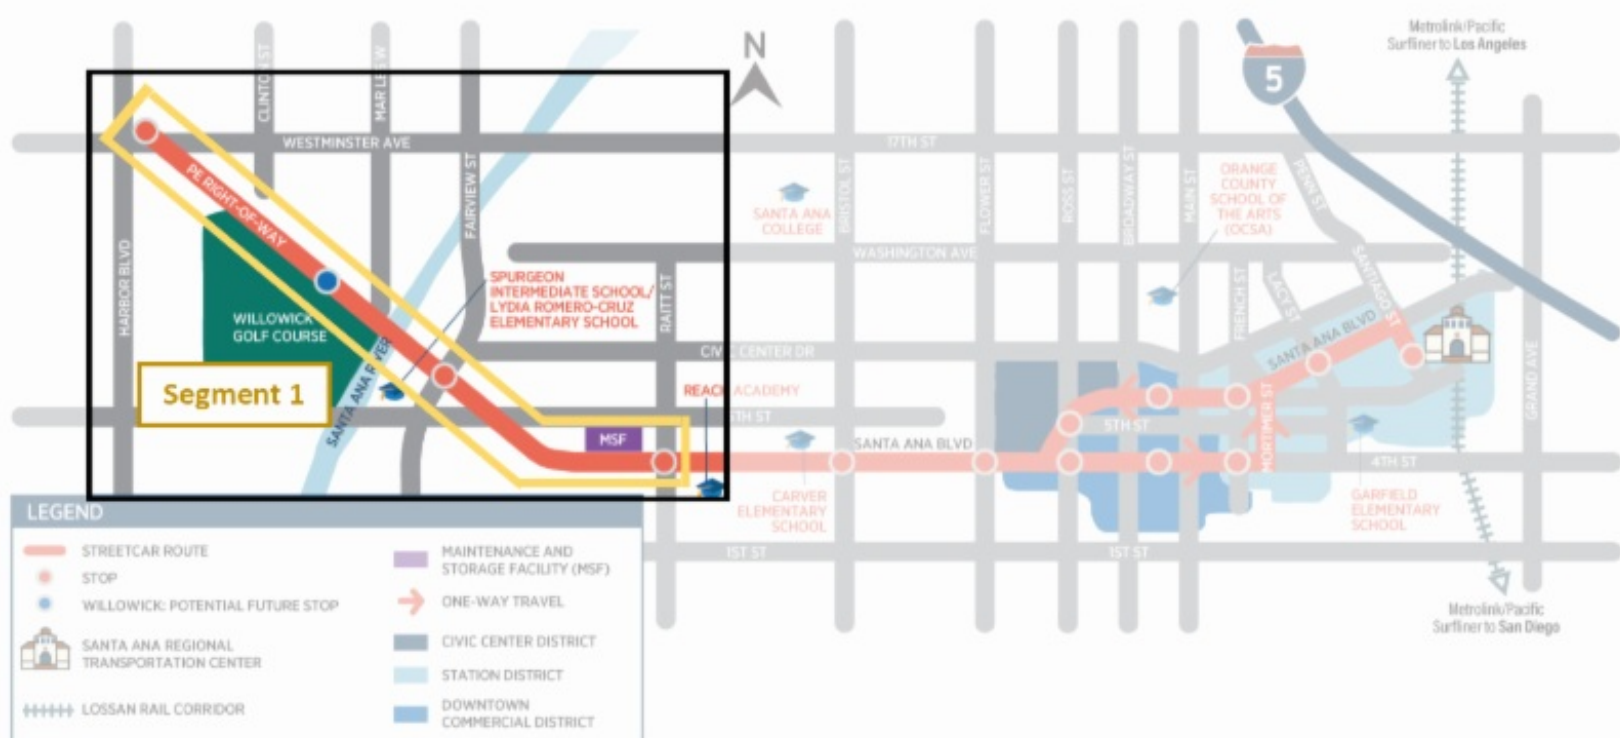


SEGMENT 2 CONSTRUCTION ACTIVITIES

Raitt St. to Parton St.

Over the next two weeks, Segment 2 construction activities will include:

- Sanitary sewer installation from N. Raitt Street to N. Bristol Street
- Tree stump grinding along Santa Ana Boulevard


Sewer installation work will generally move west to east and will require temporary lane and parking closures on W. Santa Ana Boulevard. Advance notice will be provided to community members in the segment prior to the start of the work. If visiting residents or businesses in the work zone, please ask crews to assist you in accessing the driveways. They can pull plates over the work area to facilitate entering and exiting.

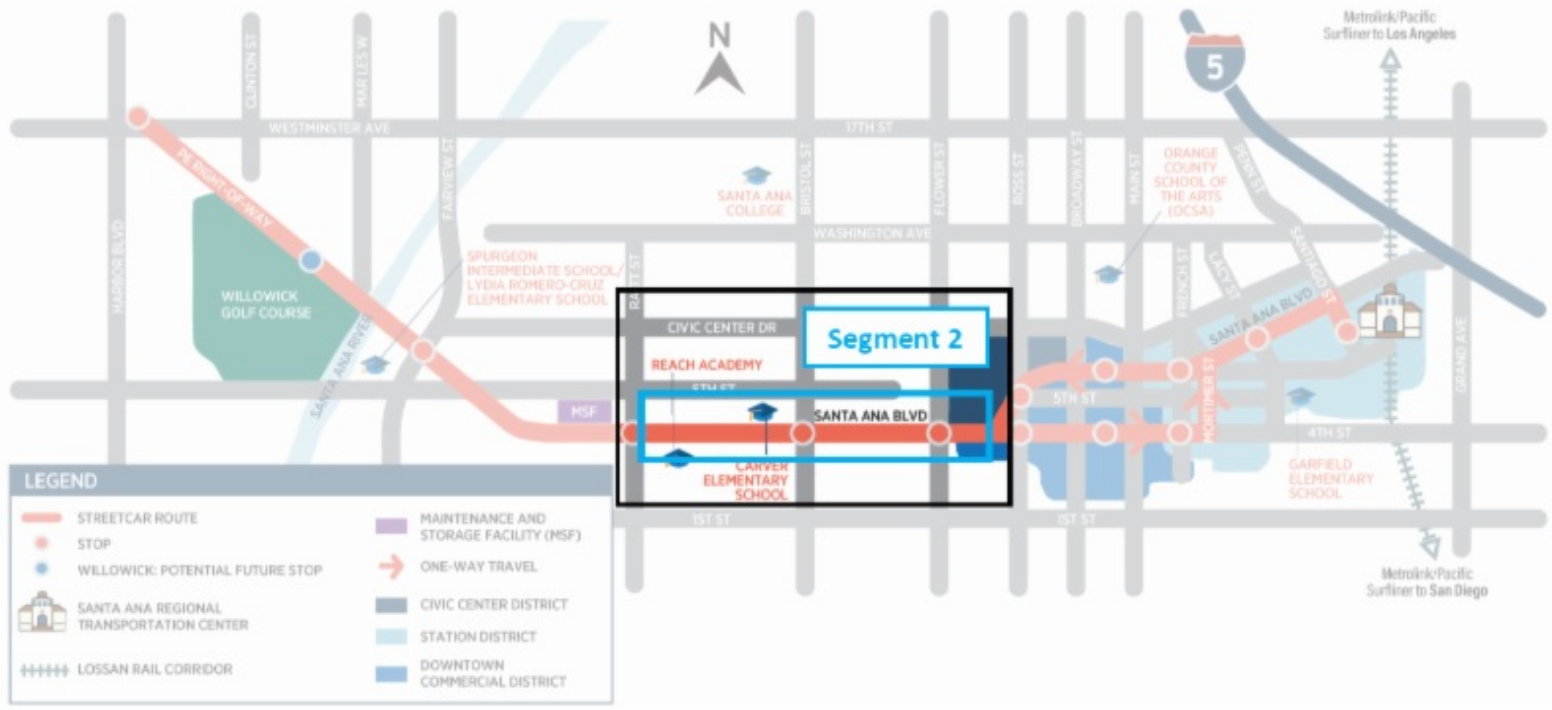

SEGMENT 3 CONSTRUCTION ACTIVITIES Ross St. to Mortimer St.


Over the next two weeks, Segment 3 construction activities will include:

- Tree stump grinding along Santa Ana Boulevard
- Water pipeline work at Sasscer Park

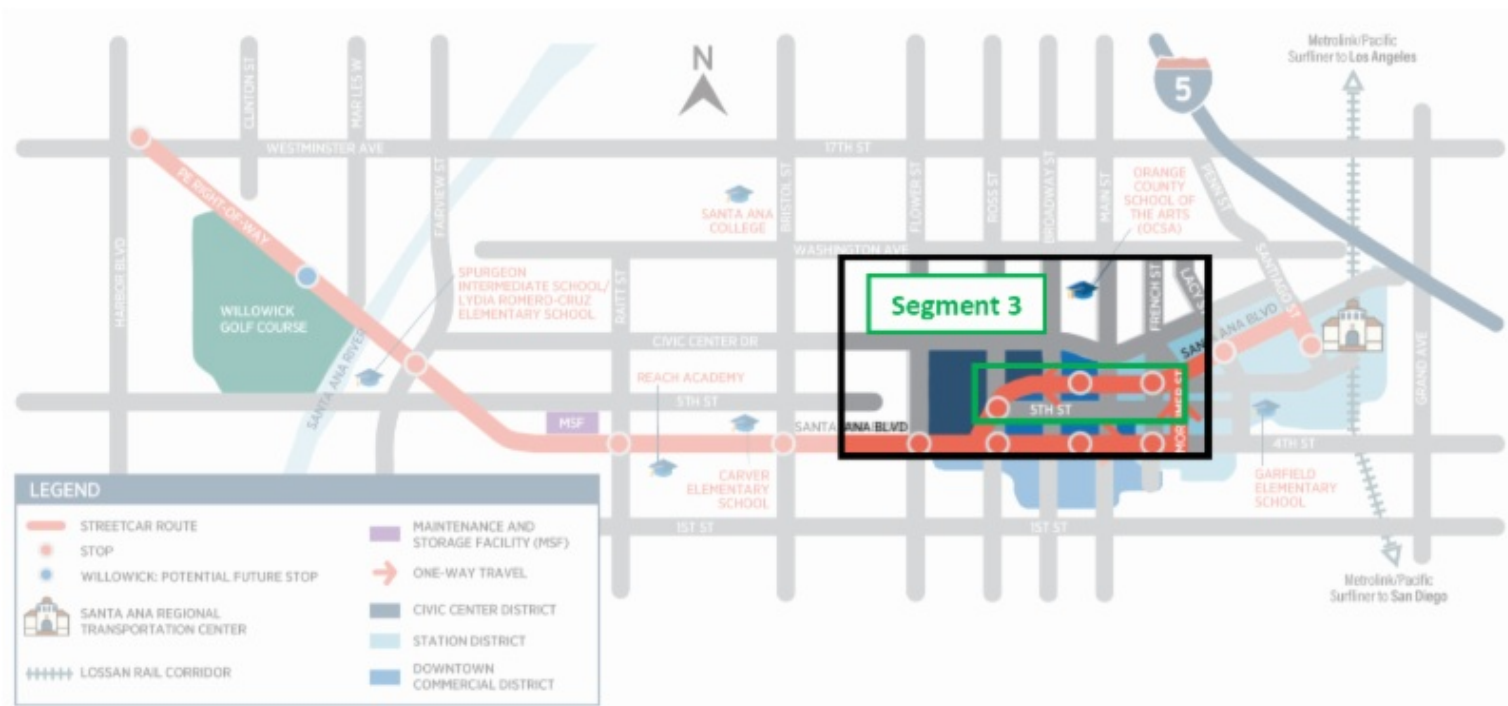


SEGMENT 4 CONSTRUCTION ACTIVITIES Ross St. to Mortimer St.

No construction activities are anticipated in Segment 4 over the next two weeks; however, utility companies are still in the area relocating their services.

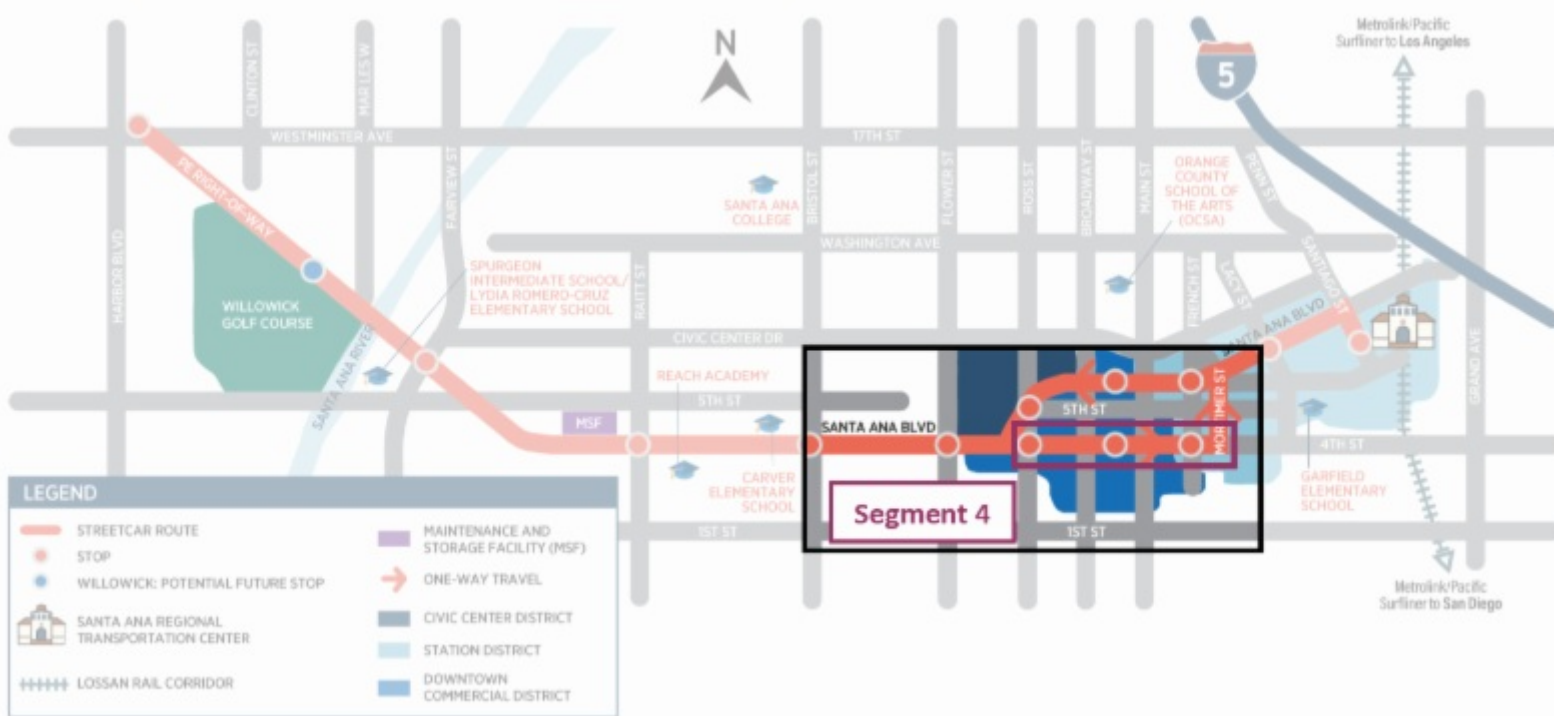

SEGMENT 5 CONSTRUCTION ACTIVITIES Mortimer St. to SARTC

No construction activities are anticipated in Segment 5 over the next two weeks.

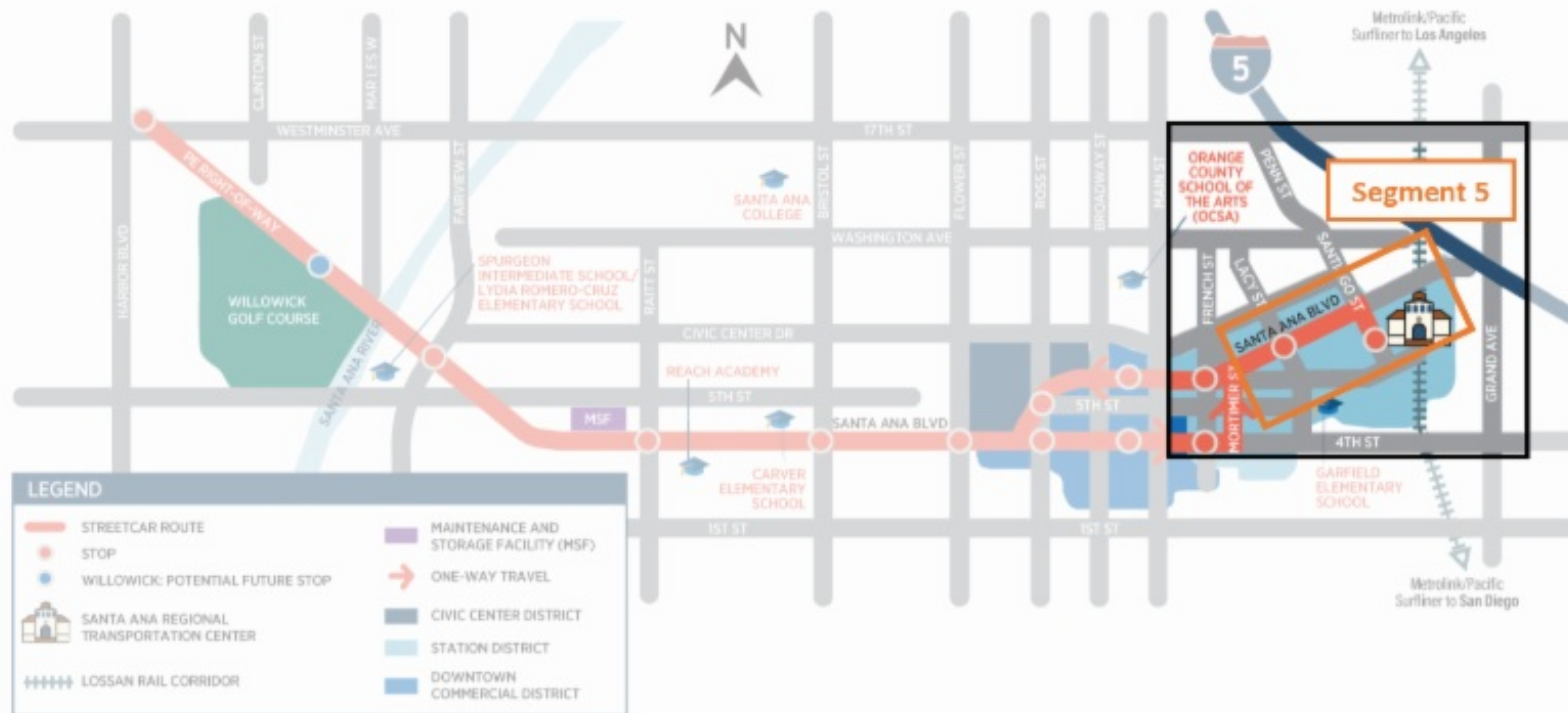




Safety of the crews and community is our top priority. Please slow down near work sites and follow pedestrian instructions.

About the Project

OC Streetcar is the first modern streetcar project to be built in Orange County and will serve Santa Ana’s historic and thriving downtown, which includes federal, state and local courthouses, government offices, colleges, an artists’ village and a thriving restaurant scene. Expected to begin carrying passengers in 2021, it will operate along a 4.15-mile route that connects the Santa Ana Regional Transportation Center (SARTC) and a new transit hub at Harbor Boulevard and Westminister Avenue in Garden Grove.

Si tiene alguna pregunta acerca del proyecto del OC Streetcar, llame a Robert Chevez al (909) 714-0172.

 OCstreetcar.com	 OCstreetcar@octa.net	 1(844) 7GO-OCSC or 1(844) 746-6272	 facebook.com/ OCstreetcar	 @OCstreetcar
---	---	---	---	---

