




Interstate 405 Improvement Project Update



Project Location and Key Features

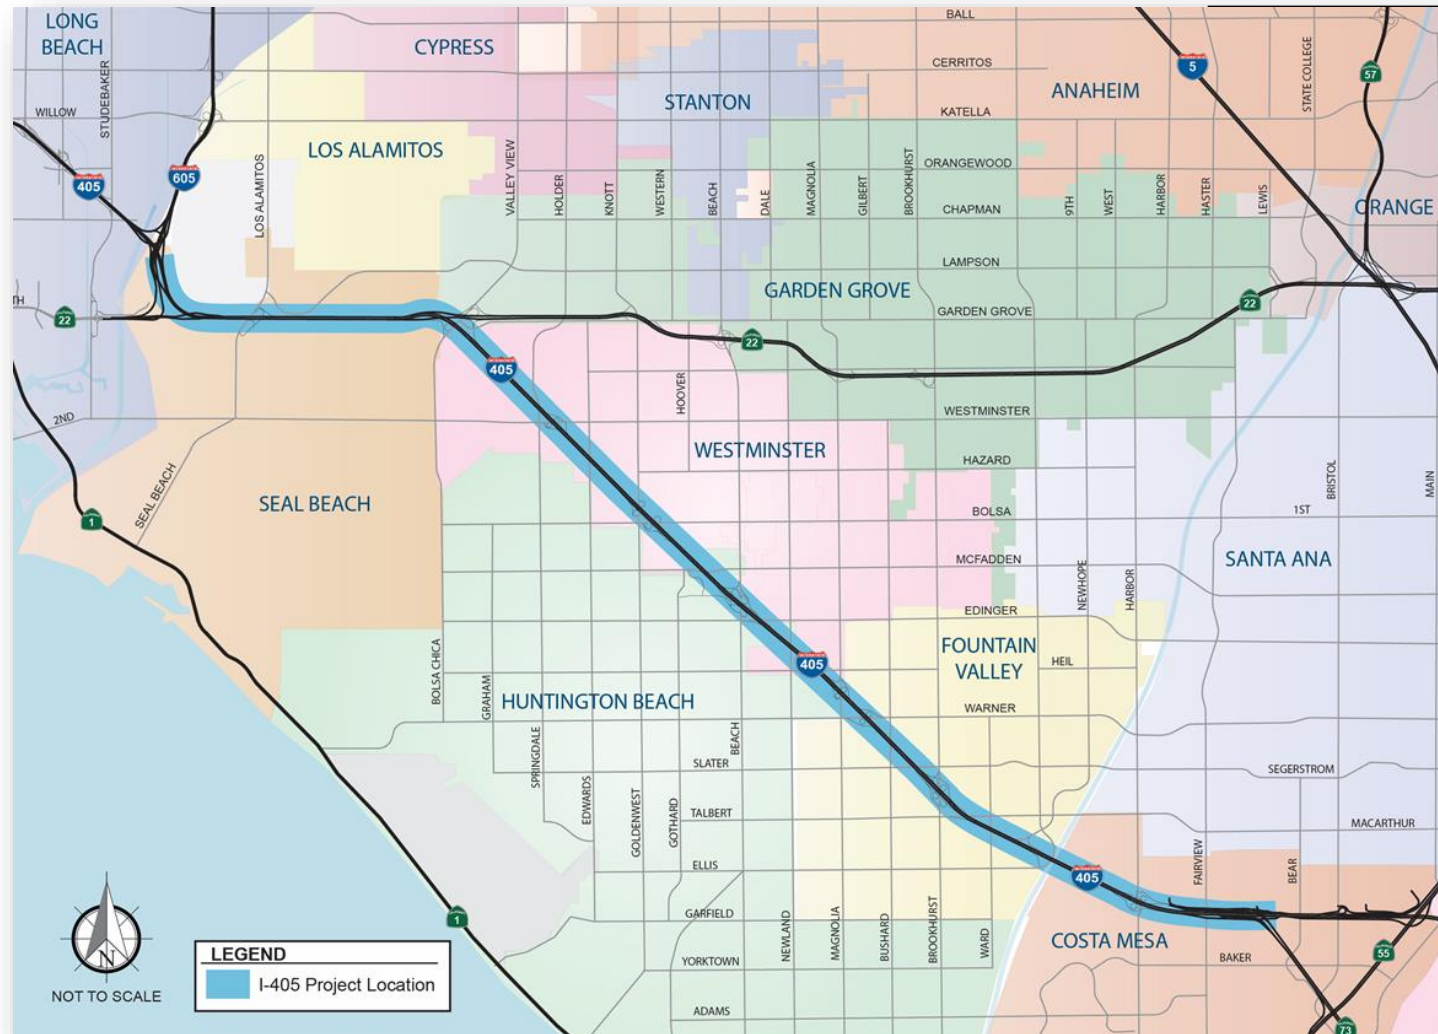

Background



- On November 14, 2016, the Orange County Transportation Authority (OCTA) Board of Directors (Board) awarded the design-build contract to OC 405 Partners (OC405)
- On January 31, 2017, OCTA executed the contract with OC405 and issued Notice to Proceed (NTP) No. 1
- On June 26, 2017, the Board approved the Transportation Infrastructure Finance and Innovation Act (TIFIA) loan
- On July 27, 2017, OCTA issued NTP No. 2 to OC405

Project Update



General

- Final baseline schedule approved
- Toll lanes system integrator under contract and working in project office
- \$165 million TIFIA loan reimbursement received in April

Design

- Project design approximately 70 percent complete
- Design anticipated to be fully complete in mid-2019

Right-of-Way

- 288 properties impacted – on schedule overall
- 248 offers presented
- 188 agreements reached (65 percent of total properties needed)
- 43 resolutions of necessity adopted by the Board

Construction Update



Re-striping



Placing k-rail

Southbound work is generally complete, northbound is more than 50 percent complete

Construction Update



Clearing and grubbing



Temporary asphalt paving

Construction Update



First utility relocation



Median concrete barrier removal

Construction Update



McFadden Avenue bridge demolition

Roadway Construction Look Ahead



- Continue freeway re-striping
- Continue installation of k-rail on outside of freeway
- Clearing and grubbing (tree and ground cover removal, etc.)
- Temporary paving
- Rough grading
- Concrete and asphalt paving and other roadway activities begin in fall

Upcoming Bridge Work



Slater Avenue (Fountain Valley)

- Single-stage bridge (closed to traffic)
- Expected to close and be demolished in late September

Goldenwest Street (Westminster)

- Two-stage bridge (open to traffic)
- 60-day settlement fill will be placed in September
- Partial demolition to follow in late November

Magnolia Street (Fountain Valley/ Westminster)

- Two-stage bridge (open to traffic)
- 60-day settlement fill will be placed in September
- Partial demolition to follow in November

Bridge Construction Map



LEGEND

- Project Limits
- Bridge Closed to Traffic During Construction
- Bridge Open to Traffic During Construction

Anticipated Start of Construction*

- 2018
- 2019
- 2020
- 2021

*Subject to Change

Open House Meetings



Please join the Orange County Transportation Authority and the California Department of Transportation to learn about the I-405 freeway construction.

There will be a presentation from 6:30 to 7 pm at each open house. Presentation topics will include a project overview, tentative bridge construction schedule, and an interactive map and Waze app demonstration.

**THURSDAY
MAY 10, 2018**

6 to 8 pm
Westminster Senior Center
8200 Westminster Boulevard
Westminster, CA 92683

**THURSDAY
MAY 31, 2018**

6 to 8 pm
Fountain Valley School District Board Room
10055 Slater Avenue
Fountain Valley, CA 92708

**THURSDAY
JUNE 7, 2018**

6 to 8 pm
Rush Park Auditorium
3021 Blume Drive
Rossmoor, CA 90720

**THURSDAY
MAY 24, 2018**

6 to 8 pm
VA Long Beach Facility
5901 E. 7th Street
Bldg 165, The Egg Auditorium
Long Beach, CA 90822

**TUESDAY
JUNE 5, 2018**

6 to 8 pm
Senior Center in Central Park
18041 Goldenwest Street
Huntington Beach, CA 92648

**THURSDAY
JUNE 14, 2018**

6 to 8 pm
Orange Coast College Student Center
2701 Fairview Road
Costa Mesa, CA 92626



STAY INFORMED

SIGN-UP TO RECEIVE PROJECT UPDATES AND ALERTS BY VISITING

www.octa.net/405improvement

Si prefiere recibir información en español, por favor llame a Evelyn French al (951) 972-2591.

Nếu bạn thích để nhận được thông tin này trong tiếng Việt, xin vui lòng liên hệ với Gia Ly (888) 662-6589.

(888) 400-8994

@405improvement

@405_Improvement

405project@octa.net

facebook.com/405improvement



Neighborhood Meetings



NEIGHBORHOOD MEETING

MCFADDEN AVENUE BRIDGE CONSTRUCTION

The Orange County Transportation Authority (OCTA) would like to invite you to attend a neighborhood meeting to learn more about the I-405 Improvement Project.
(See reverse side for locations and times)

The 405 Outreach Team will be available to answer questions regarding the upcoming McFadden Avenue bridge construction.

The McFadden Avenue bridge is tentatively scheduled for full demolition in mid- or late August 2018. The bridge will be closed during construction. Construction of the new bridge is anticipated to take approximately 12 months.
Please be advised that this work may be loud.

FOR MORE INFORMATION

	PROJECT HELP LINE:	(888) 400-8994
	PROJECT EMAIL:	405project@octa.net
	WEBSITE:	octa.net/405improvement
	FACEBOOK:	facebook.com/405improvement
	TWITTER:	@405improvement
	INSTAGRAM:	@405_improvement
	INTERACTIVE MAP:	octa.net/405map

Bilingual staff or professional interpreters will be available at the meeting.
 Si prefiere recibir información en español, por favor llame a Evelyn French al (951) 972-2501.
 Nếu quý vị muốn nhận được thông tin này bằng tiếng Việt, xin vui lòng liên lạc với cô Lý Gia (888) 662-6569.

▶ COLLEGE PARK MEETING

When: Saturday, Aug. 4, 2018
 9 to 10 a.m.

Where: College Park
 15422 Vermont St.,
 Westminster, CA 92683

▶ JOHN F. LAND SCHOOL MEETING

When: Saturday, Aug. 4, 2018
 11 a.m. to noon

Where: John F. Land School
 15151 Temple St.,
 Westminster, CA 92683
